

SOFTWARE ENGINEERING LAB 2

Agile Backlog Creation & Sprint Simulation in Jira

Scenerio: #3

Campus Placement & Internship Pipeline

Name : Shreyas K M

SRN : PES1UG24AM402

SEC : G

1. Introduction

The objective of this laboratory was to use Jira to transform functional requirements from the previous Requirements Engineering lab into an Agile backlog, organize the work into Epics and User Stories, estimate the stories using story points, run simulated Scrum sprints, and analyse progress using Jira reports.

The selected scenario is the Campus Placement & Internship Pipeline. The system supports resume parsing, eligibility screening, corporate drive configuration, placement applications, multi-round interviews, and offer management.

2. Lab 2 workflow followed

1. Create Jira Scrum project and board
2. Create Epics from major functional themes
3. Create User Stories using the end-user perspective
4. Prioritize and estimate stories
5. Create and run Sprint 1
6. Complete Sprint 1 and create/run Sprint 2
7. Generate Burndown, Sprint, Velocity and Summary reports
8. Reflect on estimation, prioritization, planning and capacity

3. Jira Project, Epics and User Stories

A Scrum board named CPP board was created under the Campus Placement Pipeline project. The placement workflow was divided into four functional themes.

Epic	Name	Purpose
E1	Resume & Eligibility Screening	Resume parsing, skill extraction, and eligibility/profile matching.
E2	Corporate Drive Management	Configuration of corporate placement drives and eligibility rules.
E3	Application & Interview Management	Applications, interview queues, and multi-round interview processing.
E4	Offer Management	Offer generation and student notification after final selection.

The screenshot displays the Jira interface for the 'CPP board' within the 'Campus Placement Pipeline' space. The board is in 'List' view and shows four work items, each representing an epic. All items are assigned to 'Shreyas K M' and have a status of 'To Do'.

Work	Assignee	Reporter	Priority	Status
CPP-1 Resume & Eligibility Screening	Unassigned	Shreyas K M	Medium	To Do
CPP-2 Corporate Drive Management	Unassigned	Shreyas K M	Medium	To Do
CPP-3 Application & Interview Management	Unassigned	Shreyas K M	Medium	To Do
CPP-4 Offer Management	Unassigned	Shreyas K M	Medium	To Do

4. User Stories and Estimation

Six user stories were created and assigned to the relevant Epics. Story points of 3, 5 and 8 were used as relative estimates following the Fibonacci-style scale described in the lab handout.

Key	User Story	Epic	Points	Priority	Sprint
CPP-5	Parse Student Resume and Extract Skills	E1	5	High	Sprint 1
CPP-6	Match Student Profile Against Eligibility Rules	E1	8	High	Sprint 1
CPP-7	Configure Corporate Placement Drive	E2	5	High	Sprint 1
CPP-8	Apply to Published Placement Drive	E3	3	High	Sprint 2
CPP-9	Manage Multi-Round Interview Process	E3	8	Medium	Sprint 2
CPP-10	Generate and Notify Student About Offer	E4	5	High	Sprint 2

5. Prioritized Backlog

The final backlog contained six User Stories. Sprint 1 focused on resume/eligibility and corporate-drive configuration, while Sprint 2 covered applications, interviews and offers.

The screenshot displays the Jira interface for the 'CPP board' (Campus Placement Pipeline). The left sidebar shows the navigation menu with options like 'For you', 'Recent', 'Starred', 'Apps', 'Plans', 'Spaces', and 'Filters'. The main content area shows the 'Backlog' view with a search bar and filters. The backlog contains six work items, each with a title, a category label, a status, and an estimate. A notification at the bottom indicates that a story 'CPP-10' has been created.

Item	Title	Category	Status	Estimate
CPP-5	Parse Student Resume and Extract Skills	Resume & Eligibilit...	To Do	5
CPP-6	Match Student Profile Against Eligibility Rules	Resume & Eligibilit...	To Do	8
CPP-7	Configure Corporate Placement Drive	Corporate Drive M...	To Do	5
CPP-8	Apply to Published Placement Drive	Application & Inter...	To Do	3
CPP-9	Manage Multi-Round Interview Process	Application & Inter...	To Do	8
CPP-10	Generate and Notify Student About Offer	Offer Management	To Do	5

6. Sprint 1 Execution

Sprint 1 contained CPP-5, CPP-6 and CPP-7 with a total commitment of 18 story points.

The screenshot displays the Jira interface for the 'CPP board' within the 'Campus Placement Pipeline' space. The 'Backlog' tab is selected, showing a list of work items. The top section, 'CPP Sprint 1', contains three items: CPP-5 (Parse Student Resume and Extract Skills, 5 points), CPP-6 (Match Student Profile Against Eligibility Rules, 8 points), and CPP-7 (Configure Corporate Placement Drive, 5 points). The total estimate for the sprint is 18 points. The bottom section, 'Backlog', contains three items: CPP-8 (Apply to Published Placement Drive, 3 points), CPP-10 (Generate and Notify Student About Offer, 5 points), and CPP-9 (Manage Multi-Round Interview Process, 8 points). The total estimate for the backlog is 16 points. A toolbar at the bottom indicates that 3 items are selected, with options to select all, edit fields, change status, merge, watch options, and delete.

Item	Summary	Category	Status	Points
CPP-5	Parse Student Resume and Extract Skills	Resume & Eligibilit...	To Do	5
CPP-6	Match Student Profile Against Eligibility Rules	Resume & Eligibilit...	To Do	8
CPP-7	Configure Corporate Placement Drive	Corporate Drive M...	To Do	5
CPP-8	Apply to Published Placement Drive	Application & Inter...	To Do	3
CPP-10	Generate and Notify Student About Offer	Offer Management	To Do	5
CPP-9	Manage Multi-Round Interview Process	Application & Inter...	To Do	8

CPP Sprint 1 - CPP board - Sc... x +

shreyas-k-m.atlassian.net/jira/software/c/projects/_CPP/boards/3?sprintStarted=true

Jira

Search

+ Create

See plans

Update

Spaces / Campus Placement Pipeline

CPP board

Summary List Active sprints Backlog Development Forms Timeline Docs Reports +

Search board

Version

Epic

Quick filters

Complete sprint

Group: Story

TO DO 2

Match Student Profile Against Eligibility Rules

Resume & Eligibility Screening

CPP-6 8

Configure Corporate Placement Drive

Corporate Drive Management

CPP-7 5

+ Create

IN PROGRESS 1

Parse Student Resume and Extract Skills

Resume & Eligibility Screening

CPP-5 5

IN REVIEW

DONE 0

CPP Sprint 1 - CPP board - Sc... x +

shreyas-k-m.atlassian.net/jira/software/c/projects/_CPP/boards/3?sprintStarted=true

Jira

Search

+ Create

See plans

Update

Spaces / Campus Placement Pipeline

CPP board

Summary List Active sprints Backlog Development Forms Timeline Docs Reports +

Search board

Version

Epic

Quick filters

Complete sprint

Group: Story

TO DO

+ Create

IN PROGRESS

+ Create

IN REVIEW

DONE 3

Parse Student Resume and Extract Skills

Resume & Eligibility Screening

CPP-5 5

Match Student Profile Against Eligibility Rules

Resume & Eligibility Screening

CPP-6 8

Configure Corporate Placement Drive

Corporate Drive Management

CPP-7 5

7. Sprint 2 Execution

Sprint 2 contained CPP-8, CPP-9 and CPP-10 with a total commitment of 16 story points.

This screenshot shows the Jira Backlog view for the 'CPP board' under the 'Campus Placement Pipeline' space. The 'CPP Sprint 2' (8 Sep - 15 Sep) is active, containing 3 work items with a total estimate of 16 story points. The items are:

Item	Story Points	Status
CPP-8: Apply to Published Placement Drive	3	To Do
CPP-10: Generate and Notify Student About Offer	5	To Do
CPP-9: Manage Multi-Round Interview Process	8	To Do

The backlog below the sprint is empty. A notification bar at the bottom indicates '3 selected' and provides options like 'Select all', 'Edit fields', 'Change status', 'Merge', 'Watch options', and 'Delete'.

This screenshot shows the Jira 'Active sprints' view for the 'CPP board'. The 'CPP Sprint 2' is active, and the board is filtered to show only the items in the current sprint. The items are organized into columns: 'TO DO' (3 items), 'IN PROGRESS' (0 items), 'IN REVIEW' (0 items), and 'DONE' (0 items).

Column	Item	Story Points	Status
TO DO	Apply to Published Placement Drive	3	To Do
	Generate and Notify Student About Offer	5	To Do
	Manage Multi-Round Interview Process	8	To Do
IN PROGRESS			
IN REVIEW			
DONE			

A notification banner at the bottom left states: 'Sprint started. We've filtered the board to show your new sprint. Good luck, team!'.

CPP Sprint 2 - CPP board - Sc

+

< > ↺ 📖

shreyas-k-m.atlassian.net/jira/software/c/projects/ CPP /boards/3?sprintStarted=true

🔥 ⚙️ ⬇️ 📄 ⚡ Update

Jira

🔍 Search

+ Create

💎 See plans

🔔

?

⚙️

SM

👤 For you

🕒 Recent >

☆ Starred >

🧩 Apps

📅 Plans

🔗 Spaces + ...

★ Starred

🔗 (Example) Billing System Dev

Recent

👤 Campus Placement Pipeline + ...

Recent

📅 CPP board

👤 My Software Team

☰ More spaces >

Recommended

🔗 Collect requests Try

☰ Filters

📊 Dashboards

👤 Teams

🎯 Goals

🔗 Projects

⚙️ Customise sidebar

Spaces / Campus Placement Pipeline

CPP board

...

🌐 Summary 📅 List 📅 Active sprints 📅 Backlog 📄 Development 📄 Forms 📅 Timeline 📄 Docs 📄 Reports +

🔍 Search board

SM 👤

Version ▾

Epic ▾

Quick filters ▾

Complete sprint

🔔

Group: Story

🔗

📄

...

TO DO

+ Create

IN PROGRESS

+ Create

IN REVIEW

DONE 3 📄

+ Add

Apply to Published Placement Drive

📄 Application & Interview Manage...

☑ CPP-8 3 ⬇️ 👤

Generate and Notify Student About Offer

📄 Offer Management

☑ CPP-10 5 ⬇️ 👤


Manage Multi-Round Interview Process

📄 Application & Interview Manage...

☑ CPP-9 8 = 👤


8. Burndown and Sprint Results

The Burndown Chart records planned work and remaining story points. In the completed sprint shown in Jira, remaining work reached zero.

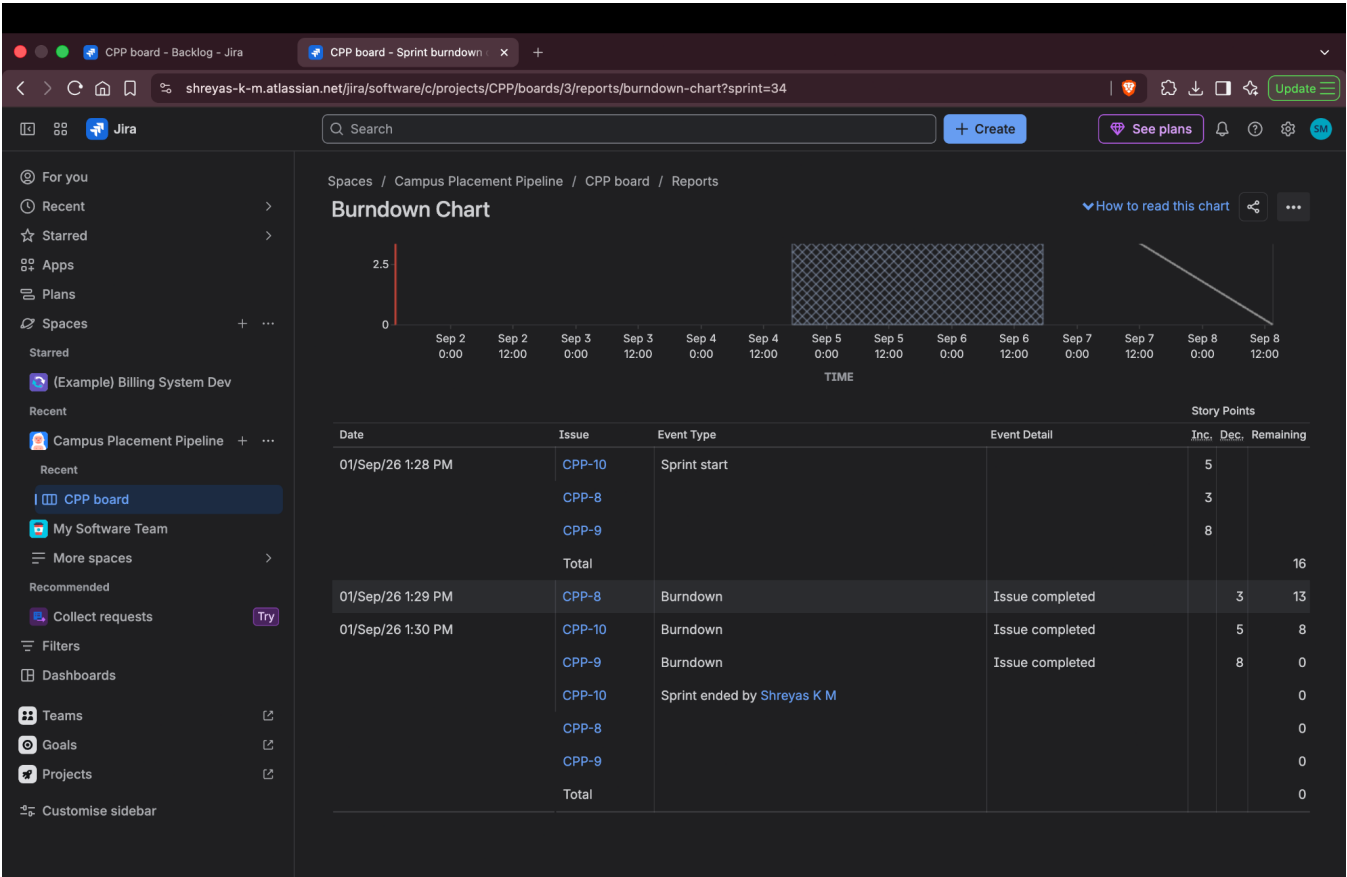


9. Sprint Report

The Sprint Report confirms completion of CPP-8, CPP-9 and CPP-10 for a total of 16 story points.

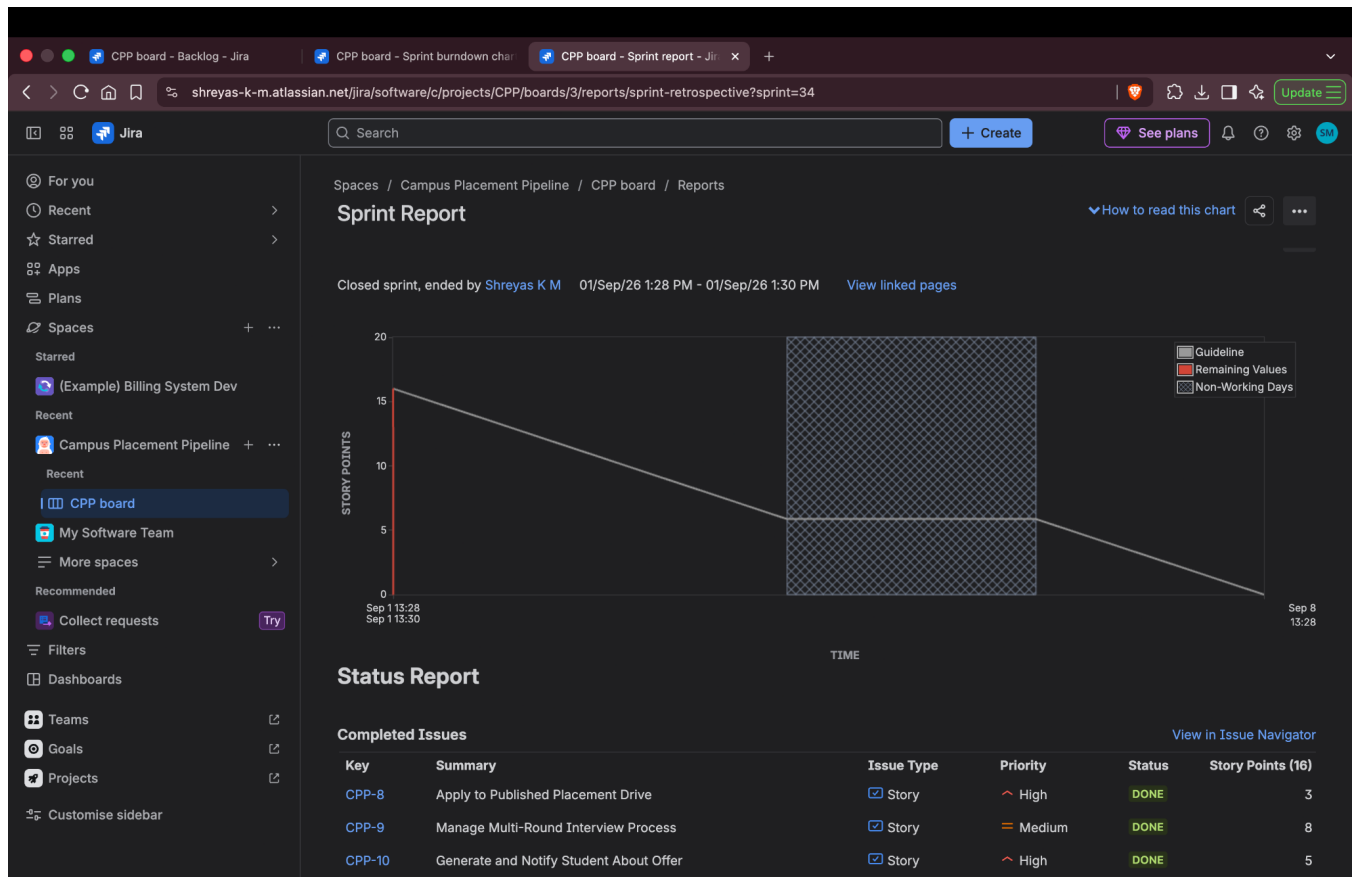


10. Velocity Report

Sprint 1 committed and completed 18 points. Sprint 2 committed and completed 16 points. Jira therefore reports an average velocity of 17 story points across the two shown sprints.

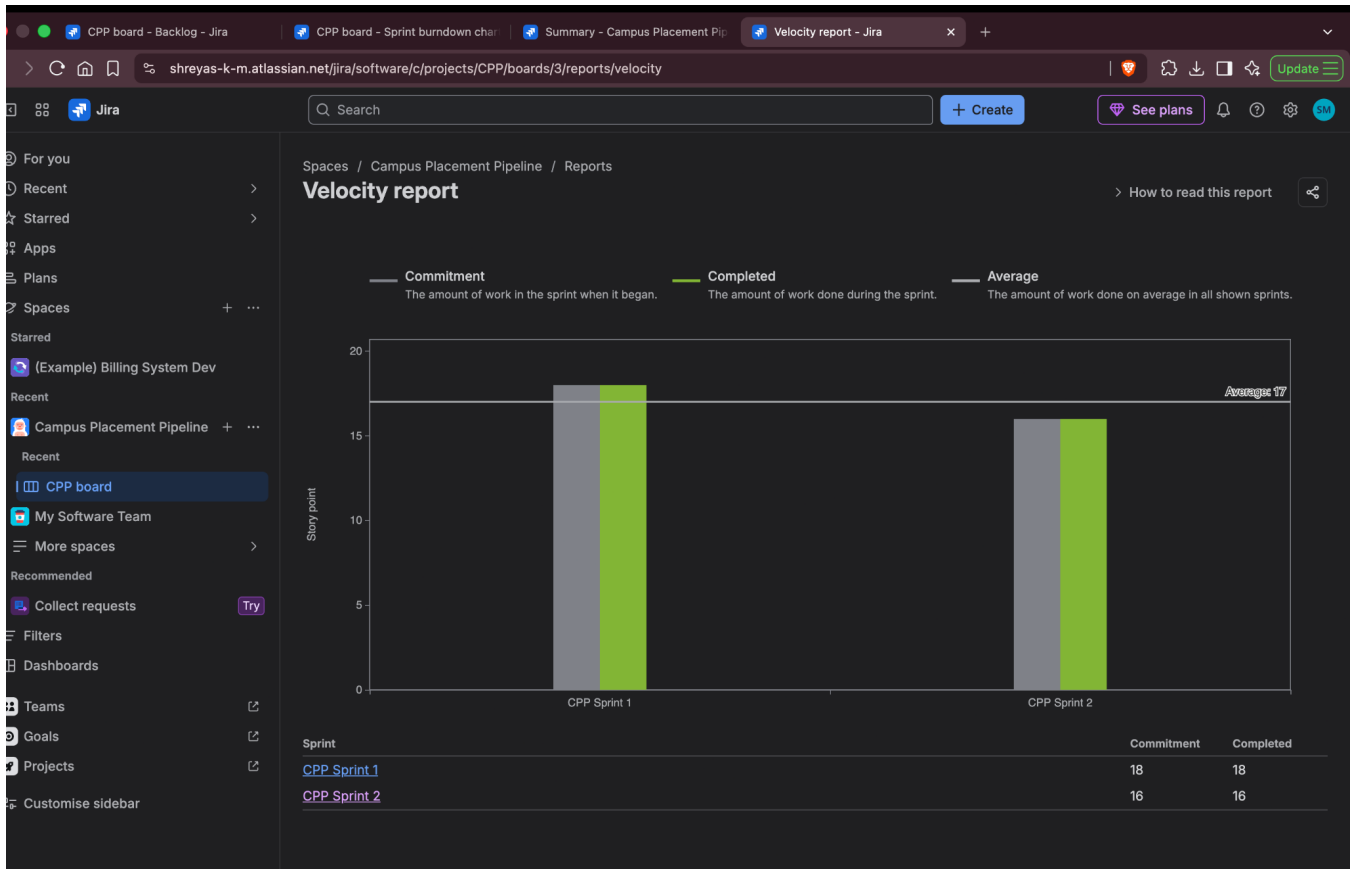

11. Jira Summary Dashboard

The Summary dashboard showed 10 total work items, 6 completed and 4 To Do at the time of capture. It also displayed recent activity, priority distribution and work-item types.

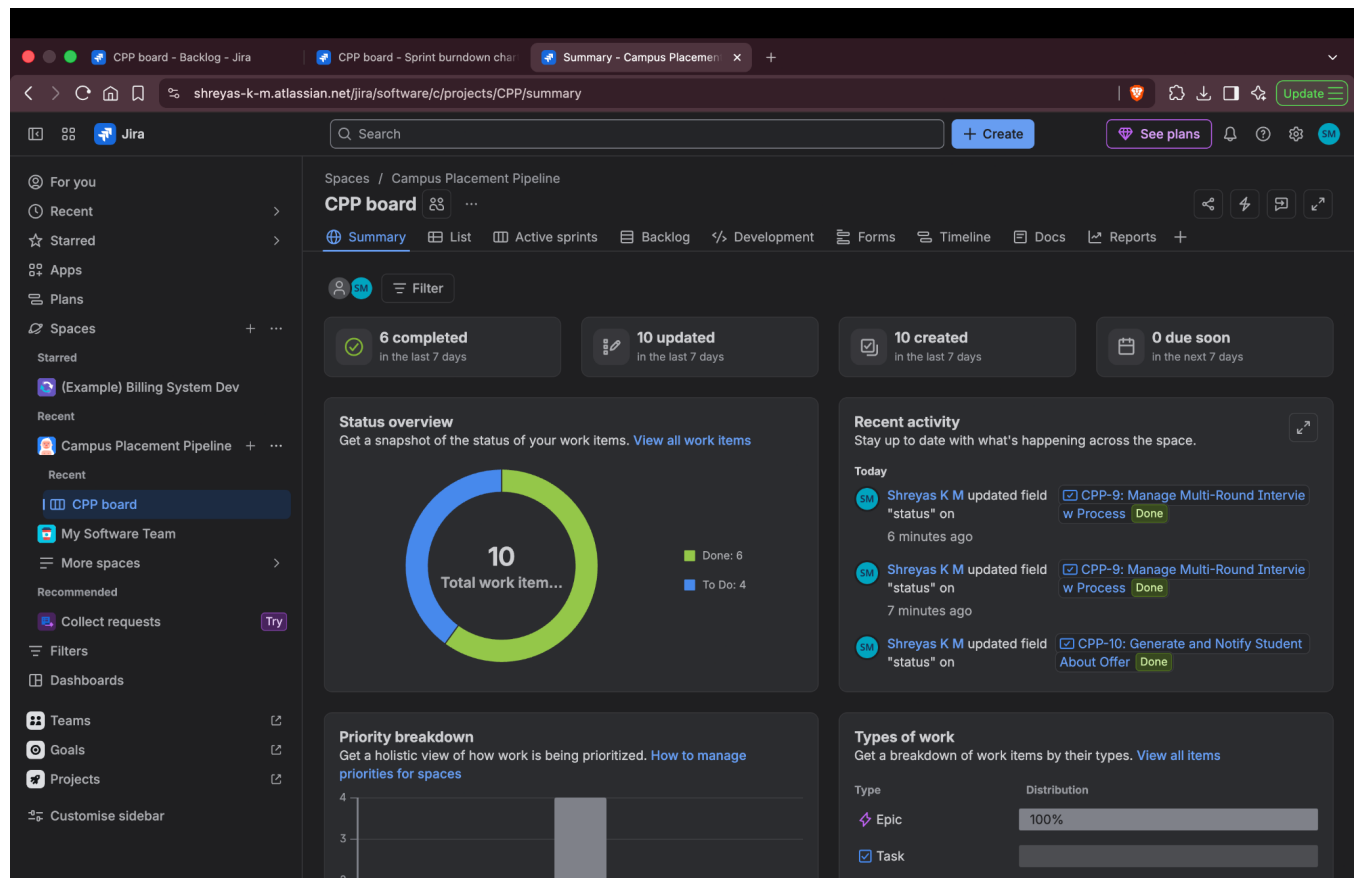

12. Reflection and Analysis

1. Did the estimations reflect the actual effort?

The estimates were usable for planning because all selected stories were completed within their respective simulated sprints. However, this was a simulated exercise and the stories were completed very quickly, so the result cannot be treated as real-world validation of effort or duration. The relative estimates were sufficient for organizing the sprint commitments.

2. Was the backlog well-prioritized?

Yes. The backlog was organized as a logical placement pipeline: resume and eligibility screening, drive configuration, application, interview management and offer management. High-priority items covered the major placement functions, while interview management was Medium.

3. How did the simulated sprint align with the plan?

The execution aligned with the planned commitments. Sprint 1 completed 18 of 18 committed story points, and Sprint 2 completed 16 of 16. All six stories were completed.

4. What insights did the Burndown Chart give about team capacity?

Both completed sprints reached zero remaining work. Across the two simulated sprints, Jira reports an average velocity of 17 story points. This can be used as a rough planning reference for this exercise, while recognizing that only two simulated sprints were observed.

14. Conclusion

The Jira-based Agile exercise successfully converted the Campus Placement & Internship Pipeline requirements into a structured backlog, four Epics and six User Stories. The stories were estimated using story points and delivered through two simulated sprints.

Both sprint commitments were completed: 18/18 story points in Sprint 1 and 16/16 in Sprint 2. The velocity report gives an average of 17 story points, while the Burndown and Sprint reports provide evidence of completion and progress tracking.
